
A Better U VR — 10-Evening Build Plan

Oct 19, 2026 · @Danny Cawthorne

Prep window (now – Oct 25)

Since build time is 10 evenings, not 10 full days, anything solved before Oct 26 is time won back once the clock starts. Before the 26th:

- Confirm Meta Model API credentials are actually issued (not just the developer account) and test one real call succeeds
- Put the Quest 3S into developer mode and confirm it can sideload a build
- Install Unity with the Android/Quest build module
- Spend an hour or two on a Quest-specific "hello world" tutorial — just enough to know where scenes, GameObjects and C# scripts live before evening one
- Decide the squat-detection approach now (controller/headset motion vs. passthrough camera + SAM) — a design decision, not a coding one, and it determines what Claude Code scaffolds in advance
- Have Claude Code scaffold what doesn't need live hardware testing: the Unity project structure, the voice loop script skeleton, the Model API call wrapper — so evenings go to wiring and debugging on-device, not typing boilerplate

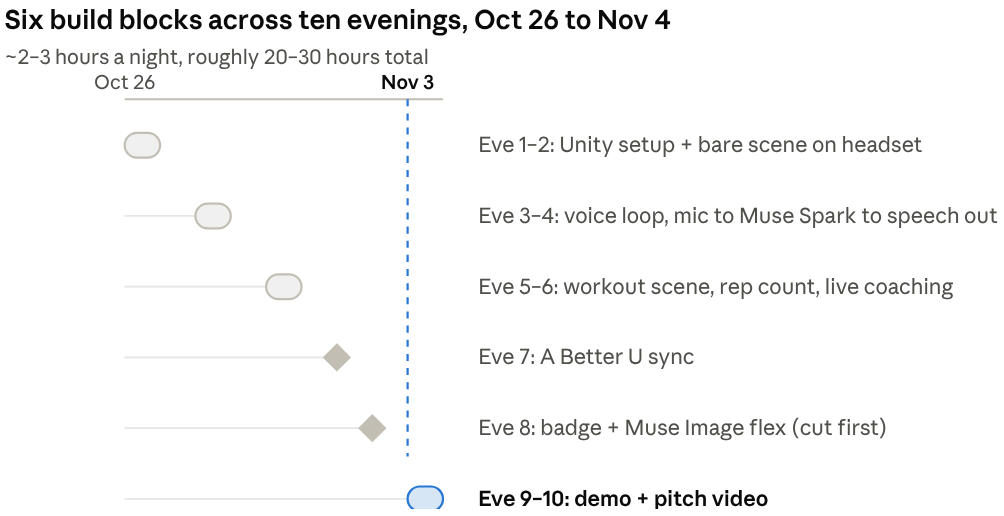

evening-by-evening build plan · 6 blocks, Oct 26 – Nov 4

The voice loop (evenings 3–4) comes before the workout scene deliberately — it's the biggest technical risk, so it needs to prove out before time is spent polishing anything around it. The demo video (evenings 9–10) matters as much as the build for judging, so it's protected time, not an afterthought squeezed in at the end.

Division of labour

Agent	Owns	Why
Claude Code	Overall architecture, Muse Spark/Meta Model API integration, A Better U account sync	Already knows the A Better U codebase and data model — stays the "brain" that understands how the VR piece fits the whole platform
Muse Code	Unity scene setup, C# wiring inside Unity, Quest CLI builds and deployment	Meta's own tooling for Meta's own hardware — likely sharpest on Quest-specific build quirks

Work is relayed manually rather than the two talking directly: Claude Code decides what needs to happen and hands Muse Code specific, scoped instructions ("wire this script to this scene object", not open-ended asks). Output gets copied back when one agent hits something clearly in the other's lane. Picking one agent as primary per piece of work avoids ping-ponging every decision across both, which matters most given the limited evening hours.

What gets cut first if evenings run short

Given 2–3 hours a night, something will likely slip. Cut in this order, protecting the voice loop and the demo above everything else:

1. Badge unlock + Muse Image auto-flex (evening 8) — nice for the pitch, not needed to prove the core coach works
2. A Better U sync (evening 7) — can be shown as a mocked/planned integration in the demo narration if time runs out, rather than a live write
3. Form-cue sophistication — ship with simple rep counting even if SAM-based form checking isn't fully tuned

Never cut: the voice loop itself (evenings 3–4) and the demo recording (evenings 9–10) — without a working coach and a clean demo, there's nothing to submit.
